Cedar River Flood Control System (FCS) Master Plan

CEDAR RAPIDS

FLOOD | CONTROL SYSTEM

STRENGTHENING OUR COMMUNITY

June 17, 2015

How We Got Here

- ✓ 2008: Interim flood control plan and concept for permanent protection
- ✓ 2009 – 2014: Acquisition program and flood recovery
- ✓ 2012 – 2013: Lobbied for GRI funding
- ✓ 2012 – Today: Flood recovery, redevelopment and protection milestones: CRST, WPC, McGrath Amphitheatre, etc.
- ✓ **2015: Cedar River Flood Control System Master Plan**

CEDAR RAPIDS
FLOOD CONTROL SYSTEM
STRENGTHENING OUR COMMUNITY

What Council is Adopting

Flood Control System master plan to guide construction over the next 20 years.

Purpose: Define City Council direction on key policy items that will allow the design team to proceed with implementation of the Flood Control System.

The Plan Serves As:

- A fluid document; it will change over time.
- A confirmation of a $400 million project plan.
- A tool for communicating to the public and legislators.

CEDAR RAPIDS
FLOOD CONTROL SYSTEM
STRENGTHENING OUR COMMUNITY

Plan Includes

- Alignment / Protection to the 2008 flood volume
- Implementation (prioritization and construction methods)
- Property acquisition and disposition policy
- Budget
- Communication and public outreach
- Format to add revisions and future policies

CEDAR RAPIDS
FLOOD CONTROL SYSTEM
STRENGTHENING OUR COMMUNITY

Alignment

- Protects as many flood-vulnerable properties as possible.
- Levees, permanent and removable floodwalls selected to integrate with neighborhood characteristics.
- Maximized use of removable flood walls to maintain enjoyment of river.

CEDAR RAPIDS
FLOOD CONTROL SYSTEM
STRENGTHENING OUR COMMUNITY

Flood Control System Considerations

- Public input
- Environmental / historical
- Regulatory
- Public / Private utilities
- Viewsheds

Partners:

- US Army Corps of Engineers
- Iowa Department of Transportation
- Iowa Department of Natural Resources
- Iowa State Historical Preservation Office

CEDAR RAPIDS
FLOOD CONTROL SYSTEM
STRENGTHENING OUR COMMUNITY

Flood Control System

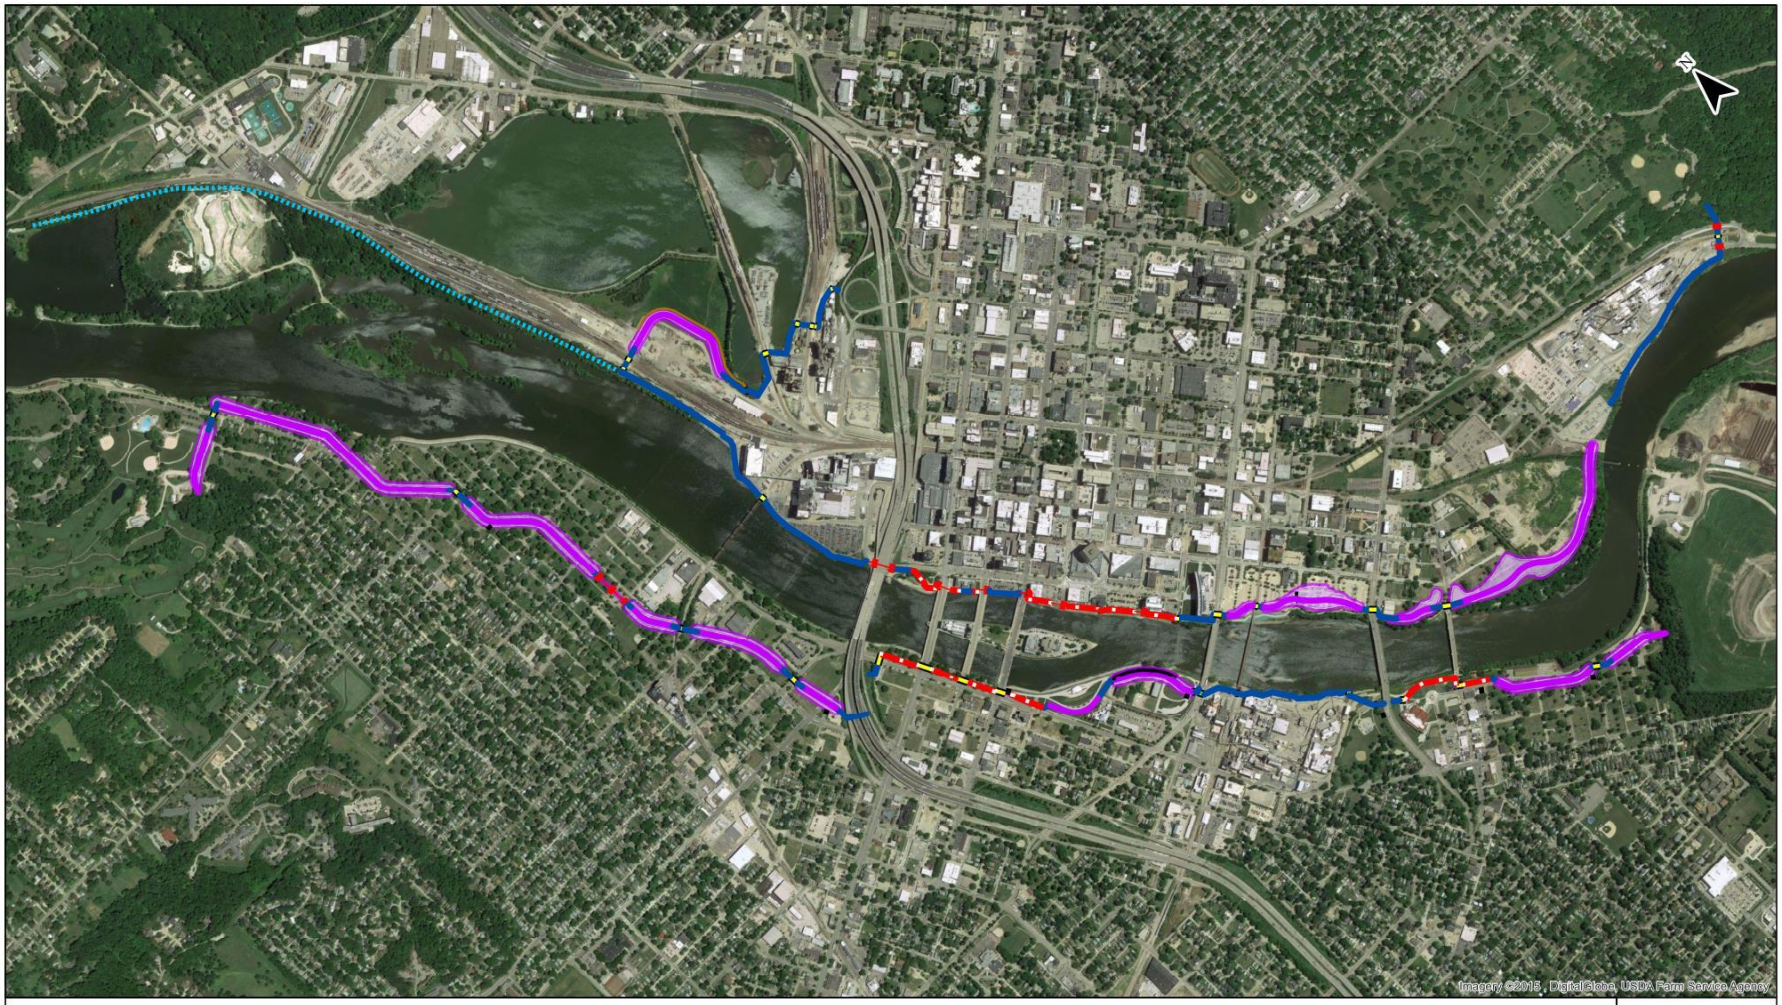

Cedar Rapids Flood Project System
East and West Side Alignment

Legend

- Gate
- Combination Wall
- Permanent Wall
- Removable Wall
- Retaining Wall
- Levee
- Alternate Cedar Lake Alignment
- Gravel Road
- Levee Footprint
- Pump Station

0 500 1,000
Feet

CEDAR RAPIDS FLOOD CONTROL SYSTEM
STRENGTHENING OUR COMMUNITY

Construction Examples

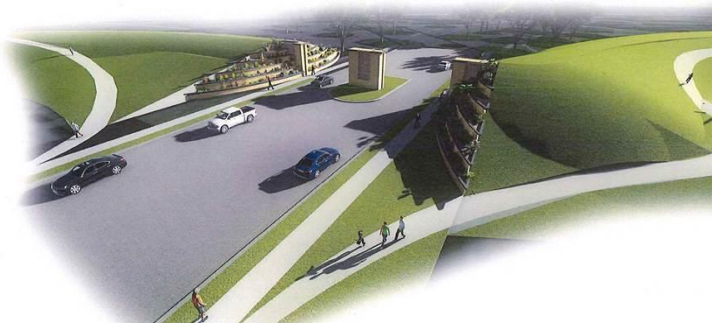

Kingston / Downtown: Permanent walls with removables above. Supports promenade.

Czech Village / NewBo / Sinclair: Levees, trails connecting to river.

Time Check: Levee upstream; permanent and combination walls.

CEDAR RAPIDS
FLOOD CONTROL SYSTEM
STRENGTHENING OUR COMMUNITY

Implementation & Sequencing

- Interim flood protection plan remains until FCS completed.
- Considerations included:
  - Interim flood risk reduction
  - Engineering
  - Social, economic, and development
- Prioritization moves between segments on both sides of river.

CEDAR RAPIDS
FLOOD CONTROL SYSTEM
STRENGTHENING OUR COMMUNITY

Sequence Plan and Reaches *	Initial Timeline
NewBo/Sinclair – from 8th Avenue Bridge to new Alliant Substation	0 – 5 years
Czech Village – from 12th Avenue Bridge to former landfill site 1	
North Industrial – from north tie-in point to Interstate 380 (I-380)	5 – 10 years
Kingston Village – from I-380 to 8th Avenue Bridge	
Downtown – from I-380 to 8th Avenue Bridge	10 + years
Time Check – from Ellis Lane (north tie-in point) to I-380	
Cargill South – from new Alliant Substation to south tie-in point	
Penford – from 8th Avenue Bridge to 12th Avenue Bridge	
Edgewood Road NW Bridge Approach	Undefined

** Sequence will change depending upon grants, development opportunities, and possibility of breaking into sub-segments.*

CEDAR RAPIDS
FLOOD CONTROL SYSTEM
STRENGTHENING OUR COMMUNITY

Acquisition Policy

- Differentiates between Mandatory and Voluntary properties for the FCS.
- Mandatory Example: Includes maintenance and operational areas.
- Voluntary Example: Downstream of FCS.
- Provides guidelines on use of flowage easements vs. total acquisitions.
- Includes “Buy Early” provision.

CEDAR RAPIDS
FLOOD CONTROL SYSTEM
STRENGTHENING OUR COMMUNITY

Disposition Policy

Includes City-owned properties:

- Unprotected (upstream and downstream of FCS)
- Project Area
- PUB Zoning – future policy addition

CEDAR RAPIDS
FLOOD CONTROL SYSTEM
STRENGTHENING OUR COMMUNITY

Budget

- Approximate 5% increase since GRI application cost estimate.

- New total cost estimate is approximately $400 Million (2015)
- With inflation, estimate is approximately $600 Million (life of project)
  - 2/3 construction
  - 1/3 design, permitting, and other pre-construction services

CEDAR RAPIDS
FLOOD CONTROL SYSTEM
STRENGTHENING OUR COMMUNITY

Communications

Public outreach will remain a critical component during the life of the FCS.

- City website, www.cedar-rapids.org
- Social media channels (Facebook, Twitter, Instagram, and YouTube)
- Online discussion board CRTalks.com
- OurCR Magazine and City Source electronic newsletter
- Stakeholder and resident outreach
- Open House: July 9 at library
- Information at public events:
  - Cedar Rapids Night at the Kernels, July 16
  - Downtown Farmer's Markets, June 6 and July 18

CEDAR RAPIDS
FLOOD CONTROL SYSTEM
STRENGTHENING OUR COMMUNITY

Special Thanks…

…to countless residents, property owners, and business leaders who invested time and attention...

Staff and consultant teams would like to thank the community for their time and involvement.

CEDAR RAPIDS

FLOOD CONTROL SYSTEM

STRENGTHENING OUR COMMUNITY
